


F3-R10b-SM-01 Asaoka Assessment


F3-R10b-SM-01 Settlement and ground level Series

Easting	Northing	Latest Reading	Ground Level	DOC
6773	23890	0.712 m	19.67 mCD	100 %

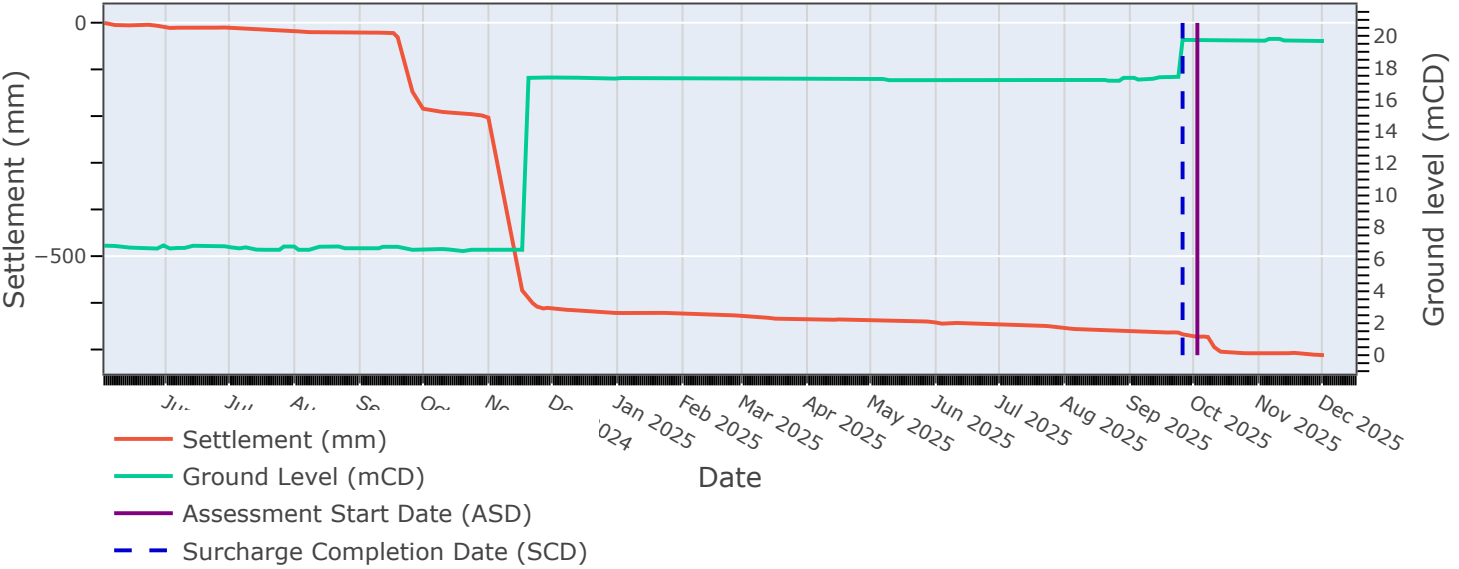

F3-R10b-SM-01 Asaoka Plot

Equation	Asaoka sf (m)	DOC (%)	Assessment From
$y = 0.572x + 303.86$	0.71	100	2025-10-03

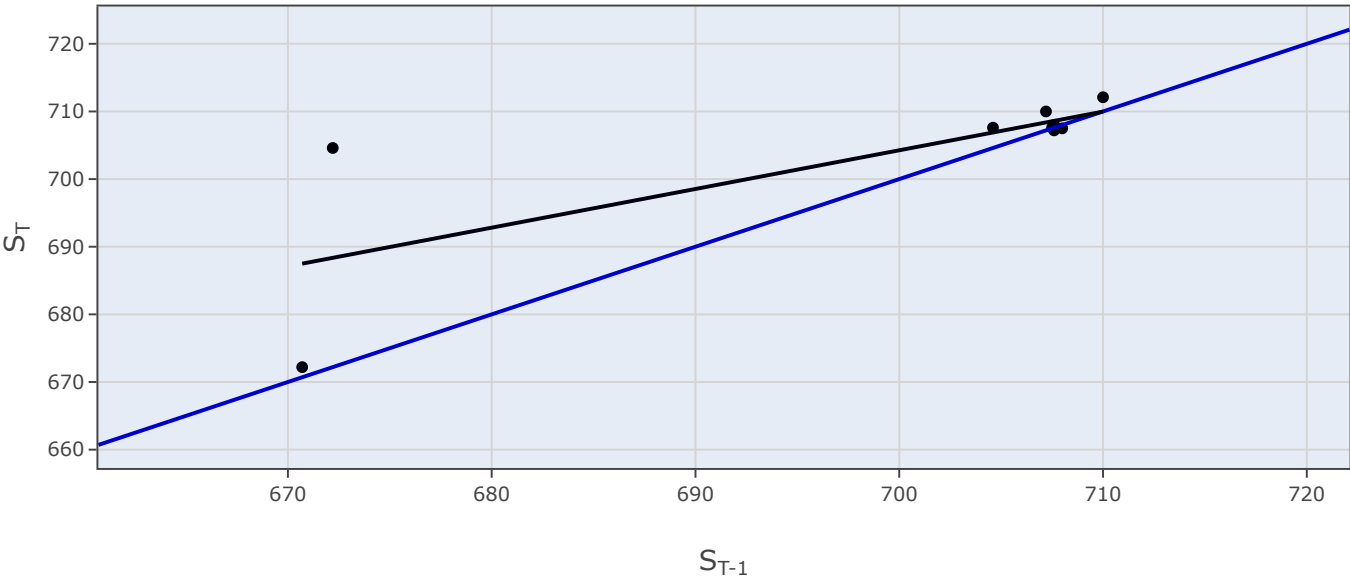


F3-R10b-SM-01 Asaoka Ordered Pairs

T	St	T-1	St-1
2025-10-06T00:00:00	672.2	2025-09-29T00:00:00	670.7
2025-10-14T00:00:00	704.6	2025-10-06T00:00:00	672.2
2025-10-21T00:00:00	707.6	2025-10-14T00:00:00	704.6
2025-10-28T00:00:00	708	2025-10-21T00:00:00	707.6
2025-11-04T00:00:00	707.5	2025-10-28T00:00:00	708
2025-11-11T00:00:00	707.6	2025-11-04T00:00:00	707.5
2025-11-18T00:00:00	707.2	2025-11-11T00:00:00	707.6
2025-11-25T00:00:00	710	2025-11-18T00:00:00	707.2
2025-12-02T00:00:00	712.1	2025-11-25T00:00:00	710

F3-R10b-SM-02 Asaoka Assessment


F3-R10b-SM-02 Settlement and ground level Series

Easting	Northing	Latest Reading	Ground Level	DOC
6813	23890	1.075 m	19.6 mCD	99.4 %

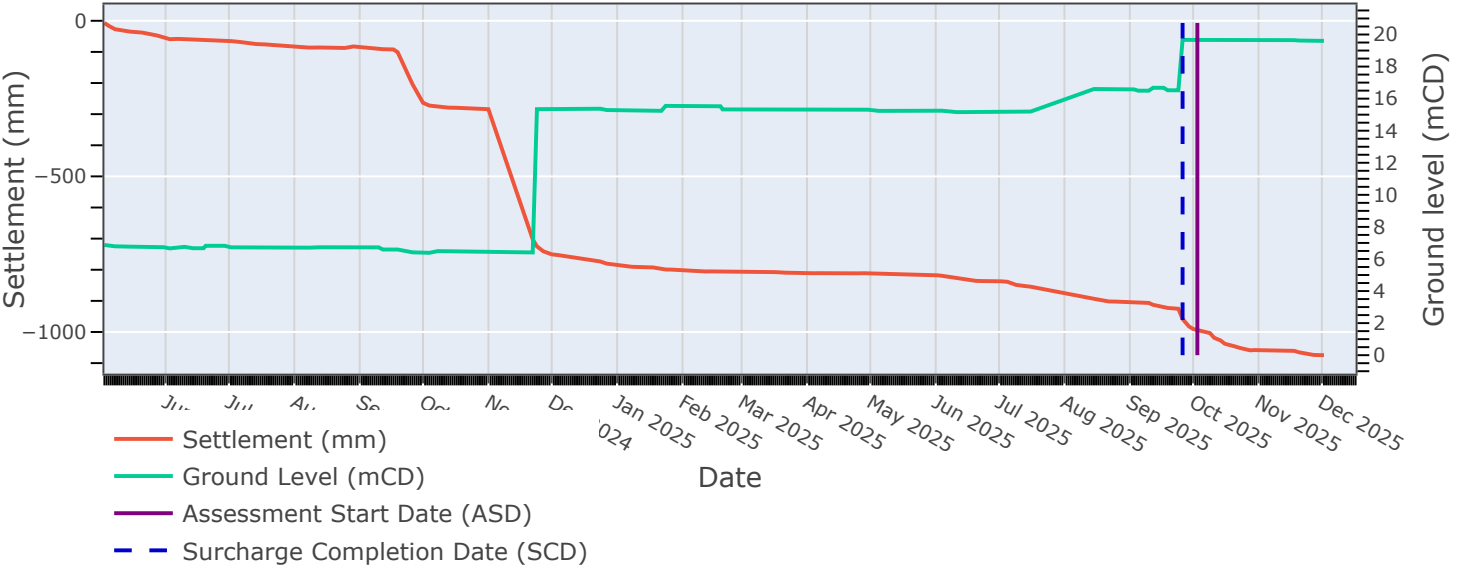

F3-R10b-SM-02 Asaoka Plot

Equation	Asaoka sf (m)	DOC (%)	Assessment From
$y = 0.746x + 274.68$	1.081	99.4	2025-10-03

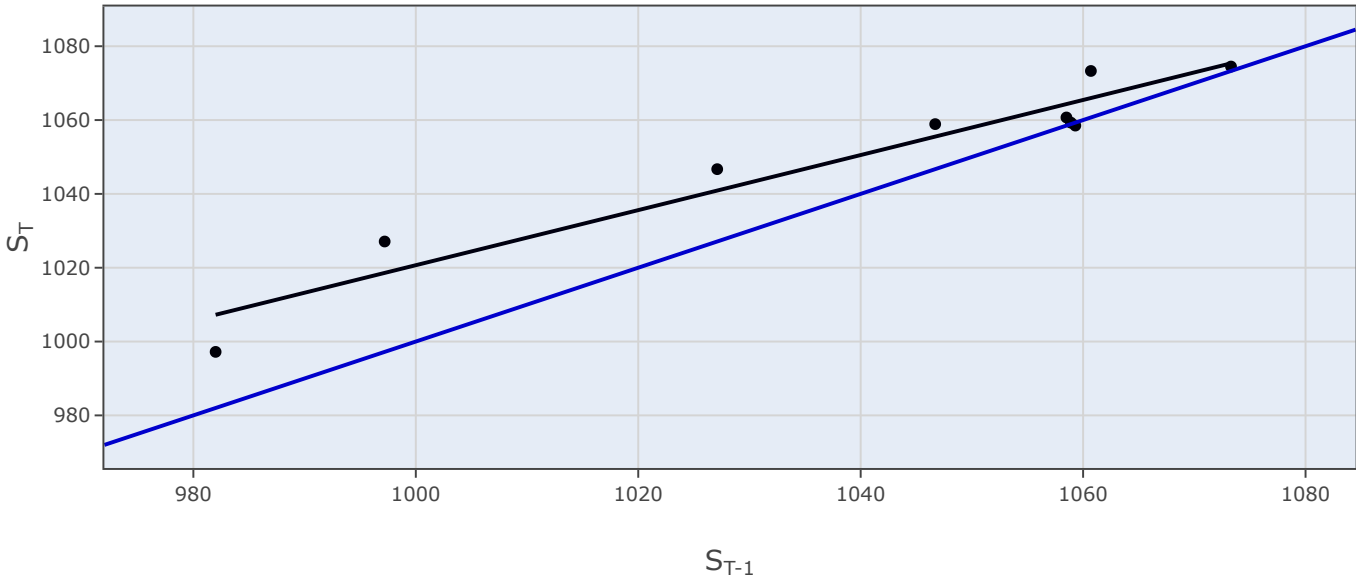


F3-R10b-SM-02 Asaoka Ordered Pairs

T	St	T-1	St-1
2025-10-06T00:00:00	997.2	2025-09-29T00:00:00	982
2025-10-14T00:00:00	1027.1	2025-10-06T00:00:00	997.2
2025-10-21T00:00:00	1046.7	2025-10-14T00:00:00	1027.1
2025-10-28T00:00:00	1058.9	2025-10-21T00:00:00	1046.7
2025-11-04T00:00:00	1059.3	2025-10-28T00:00:00	1058.9
2025-11-11T00:00:00	1058.5	2025-11-04T00:00:00	1059.3
2025-11-18T00:00:00	1060.7	2025-11-11T00:00:00	1058.5
2025-11-25T00:00:00	1073.3	2025-11-18T00:00:00	1060.7
2025-12-02T00:00:00	1074.5	2025-11-25T00:00:00	1073.3

F3-R10b-SM-03 Asaoka Assessment


F3-R10b-SM-03 Settlement and ground level Series

Easting	Northing	Latest Reading	Ground Level	DOC
6853	23890	1.216 m	19.52 mCD	99.98 %

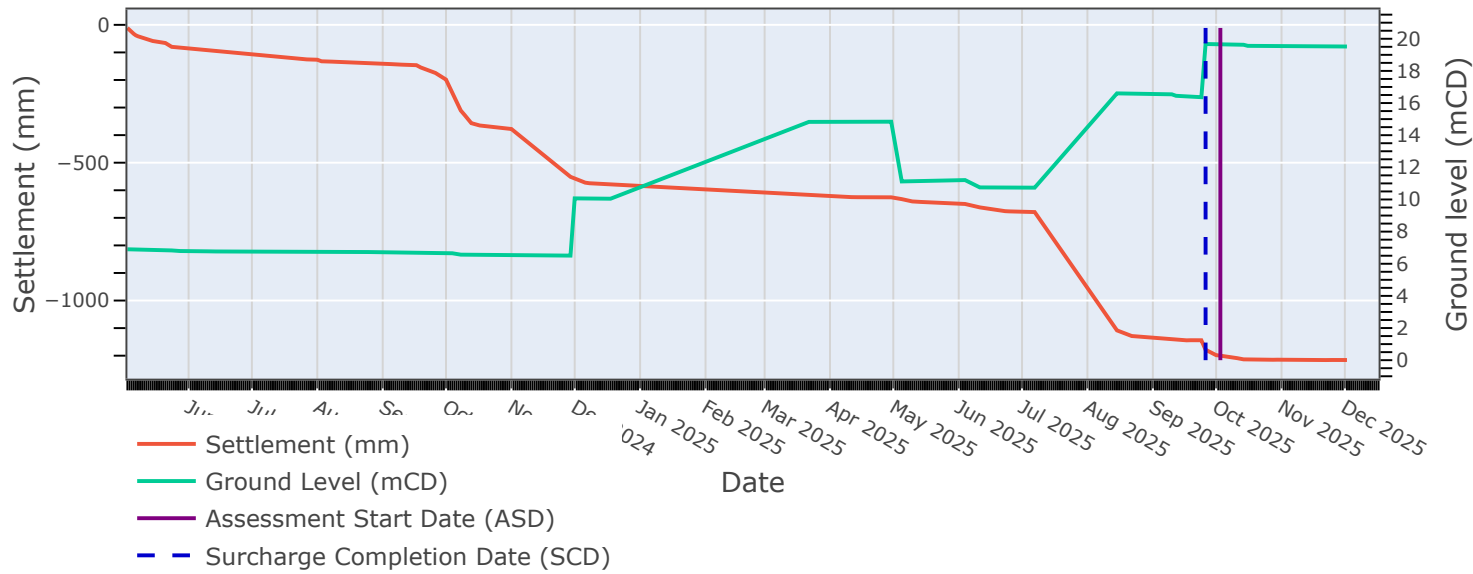

F3-R10b-SM-03 Asaoka Plot

Equation	Asaoka sf (m)	DOC (%)	Assessment From
$y = 0.514x + 591.66$	1.216	99.98	2025-10-03

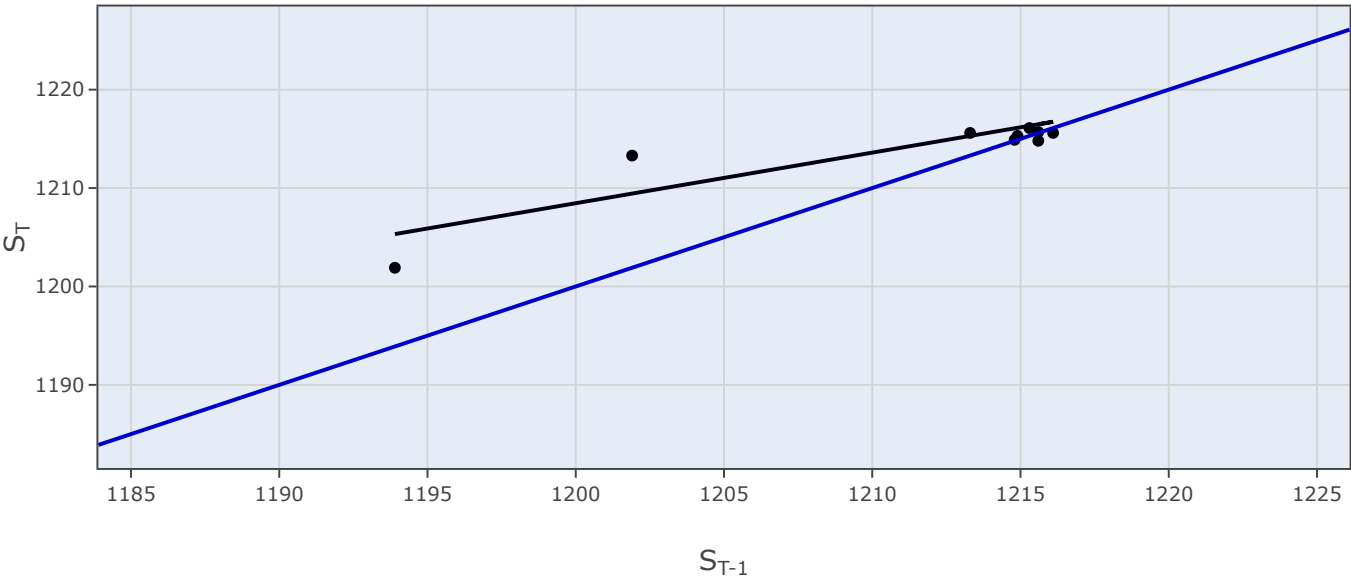


F3-R10b-SM-03 Asaoka Ordered Pairs

T	St	T-1	St-1
2025-10-06T00:00:00	1201.9	2025-09-29T00:00:00	1193.9
2025-10-14T00:00:00	1213.3	2025-10-06T00:00:00	1201.9
2025-10-21T00:00:00	1215.6	2025-10-14T00:00:00	1213.3
2025-10-28T00:00:00	1214.8	2025-10-21T00:00:00	1215.6
2025-11-04T00:00:00	1214.9	2025-10-28T00:00:00	1214.8
2025-11-11T00:00:00	1215.3	2025-11-04T00:00:00	1214.9
2025-11-18T00:00:00	1216.1	2025-11-11T00:00:00	1215.3
2025-11-25T00:00:00	1215.6	2025-11-18T00:00:00	1216.1
2025-12-02T00:00:00	1215.7	2025-11-25T00:00:00	1215.6

F3-R10b-SM-04 Asaoka Assessment


F3-R10b-SM-04 Settlement and ground level Series

Easting	Northing	Latest Reading	Ground Level	DOC
6893	23890	1.53 m	19.55 mCD	100 %

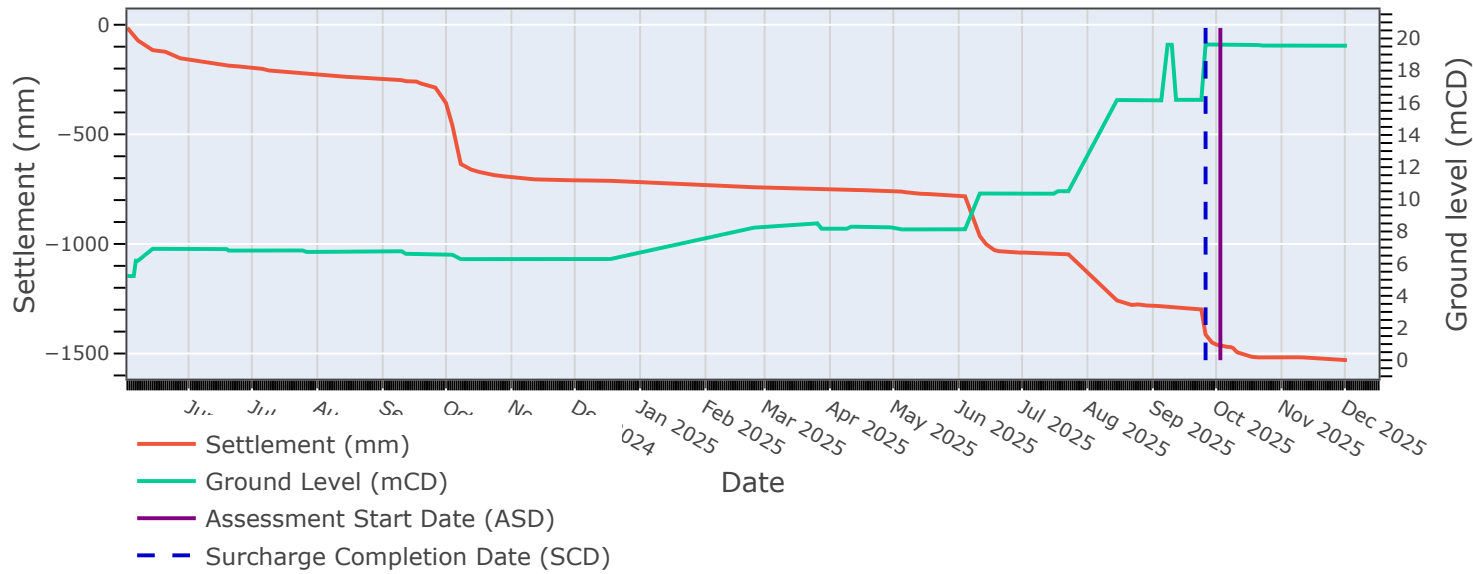

F3-R10b-SM-04 Asaoka Plot

Equation	Asaoka sf (m)	DOC (%)	Assessment From
$y = 0.627x + 570.06$	1.528	100	2025-10-03

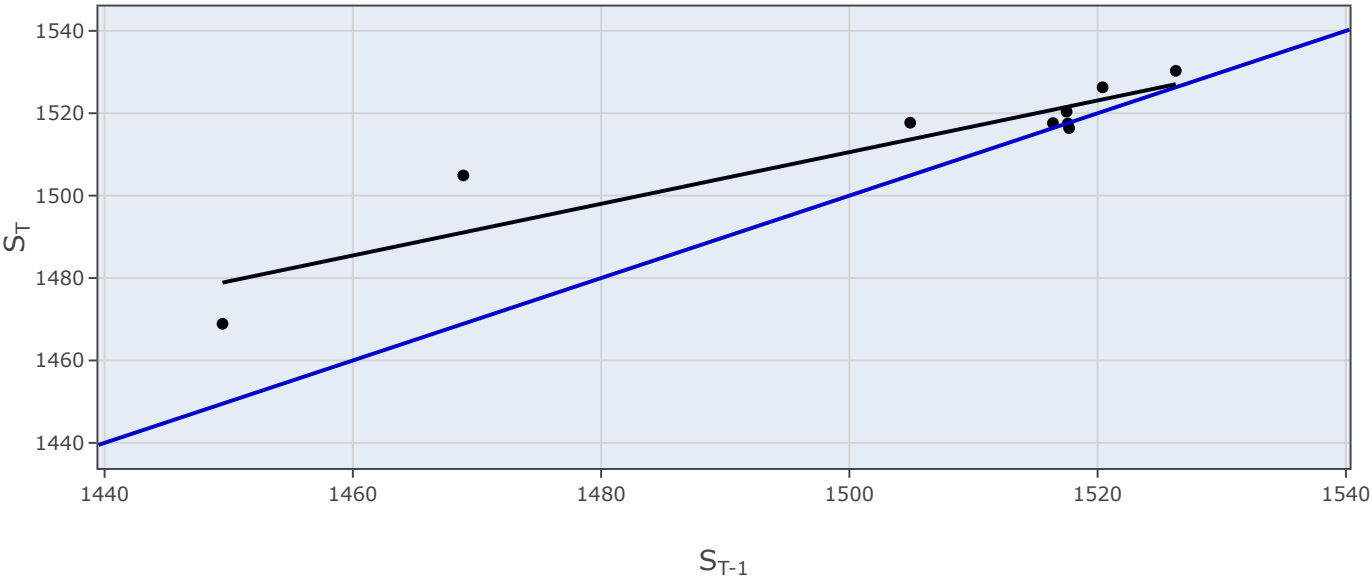

F3-R10b-SM-04 Asaoka Ordered Pairs

T	St	T-1	St-1
2025-10-06T00:00:00	1468.9	2025-09-29T00:00:00	1449.5
2025-10-14T00:00:00	1504.9	2025-10-06T00:00:00	1468.9
2025-10-21T00:00:00	1517.7	2025-10-14T00:00:00	1504.9
2025-10-28T00:00:00	1516.4	2025-10-21T00:00:00	1517.7
2025-11-04T00:00:00	1517.6	2025-10-28T00:00:00	1516.4
2025-11-11T00:00:00	1517.5	2025-11-04T00:00:00	1517.6
2025-11-18T00:00:00	1520.4	2025-11-11T00:00:00	1517.5
2025-11-25T00:00:00	1526.3	2025-11-18T00:00:00	1520.4
2025-12-02T00:00:00	1530.3	2025-11-25T00:00:00	1526.3

Asaoka Assessment Summary (data as at Week 49)

Settlement Plate	Last Read	Latest Settlement (m)	Latest GroundLevel (mCD)	Asaoka DOC (%)	Remarks
F3-R10b-SM-01	2025-12-02	0.71	19.67	100.0	OK
F3-R10b-SM-02	2025-12-02	1.07	19.6	99.4	OK
F3-R10b-SM-03	2025-12-02	1.22	19.52	99.98	OK
F3-R10b-SM-04	2025-12-02	1.53	19.55	100.0	OK
